District 3 Year 4 Project

Select a period to highlight at right. A legend describing the charting follows.

Period Highlight: 1

Plan Duration | Actual Start | % Complete | Actual (beyond Plan) | % Complete (beyond

Complete 8/31/2020

ACTIVITY	PLAN START	PLAN DURATION	ACTUAL START	ACTUAL DURATION	PERCENT COMPLETE
Notice To Proceed	5	24	0	0	0.00%
N. J St.	6	11	0	0	0.00%
8th Ave. N.	6	11	0	0	0.00%
5th Ave. N.	6	12	0	0	0.00%
Cornell Dr.	7	12	0	0	0.00%
18th Ave. N.	9	7	0	0	0.00%
N. J Terrace	10	6	0	0	0.00%
Carolina Ct.	11	7	0	0	0.00%
Duke Ct.	11	7	0	0	0.00%
North N. St.	12	9	0	0	0.00%
N. Ocean Breeze	12	9	0	0	0.00%
Pennsylvania Dr.	14	14	0	0	0.00%
Dartmouth Dr.	13	13	0	0	0.00%
N.Lakeside Dr (14th to 16th)	9	18	0	0	0.00%
14th Ave. N.	25	1	0	0	0.00%
Wellesley Dr.	8	9	0	0	0.00%
N. K St.	15	12	0	0	0.00%
N. Lakeside Dr. (7th to 9th)	15	9	0	0	0.00%
N. Lakeside Dr. (10th to 12th)	17	10	0	0	0.00%
N. L St.	17	12	0	0	0.00%
N. Palmway	10	8	0	0	0.00%
Substantial Completion	25	4	0	0	0.00%
Final Completion	0	0	0	0	0.00%

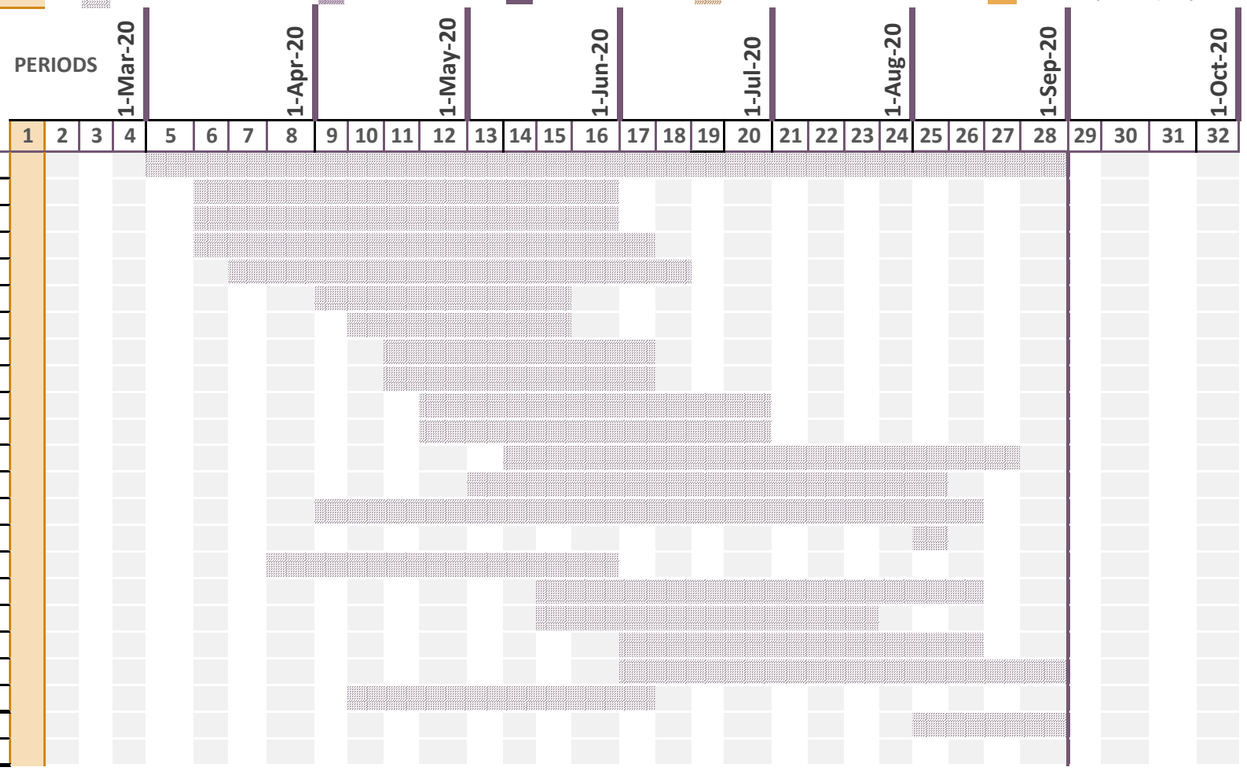

Roadway segments in project:

N. J St.. (11th Ave. N. to 12th Ave. N.)
8th Ave. N. (N. Federal Hwy to N. Ocean Breeze)
5th Ave. N. (N. Dixie Hwy. to N. J St.)
Cornell Dr. (n. Federal Hwy. to Pennsylvania Ave.)
18th Ave. N. (N. J Terrace to N. K St.)
N. J Terrace (18th Ave. N. to Wellesley Dr.)
Carolina Ct. (Maryland Dr. to dead End)

Duke Ct. (Maryland Dr. to dead End)
North N. St. (17th Ave. N. to 18th Ave. N.)
N. Ocean Breeze (16th Ave. N. to Wellesley Dr.)
Pennsylvania Dr. (Wellesley ave. to Dartmouth Dr.)
Dartmouth Dr. (Pennsylvania Ave. to N. Federal Hwy.)
N.Lakeside Dr (14th ave. N. to 16th Ave. N.)
14th Ave. N. (N. Palmway to N. Lakeside Dr.)

Wellesley Dr. (N. N St. to N. Lakeside Dr.)
N. K St. (9th ave. N. to 11th ave. N.)
N.Lakeside Dr (7th Ave. N. to 9th Ave. N.)
N.Lakeside Dr (10th Ave. N. to 12th Ave. N.)
N. L St. (9th Ave. N. to 10th Ave. N.)
N. Palmway (18th ave. N. to Wellesley Dr.)

Updated: 3/19/2020
